


HOPE UNIVERSITY COLLEGE
ADDIS ABABA
ETHIOPIA

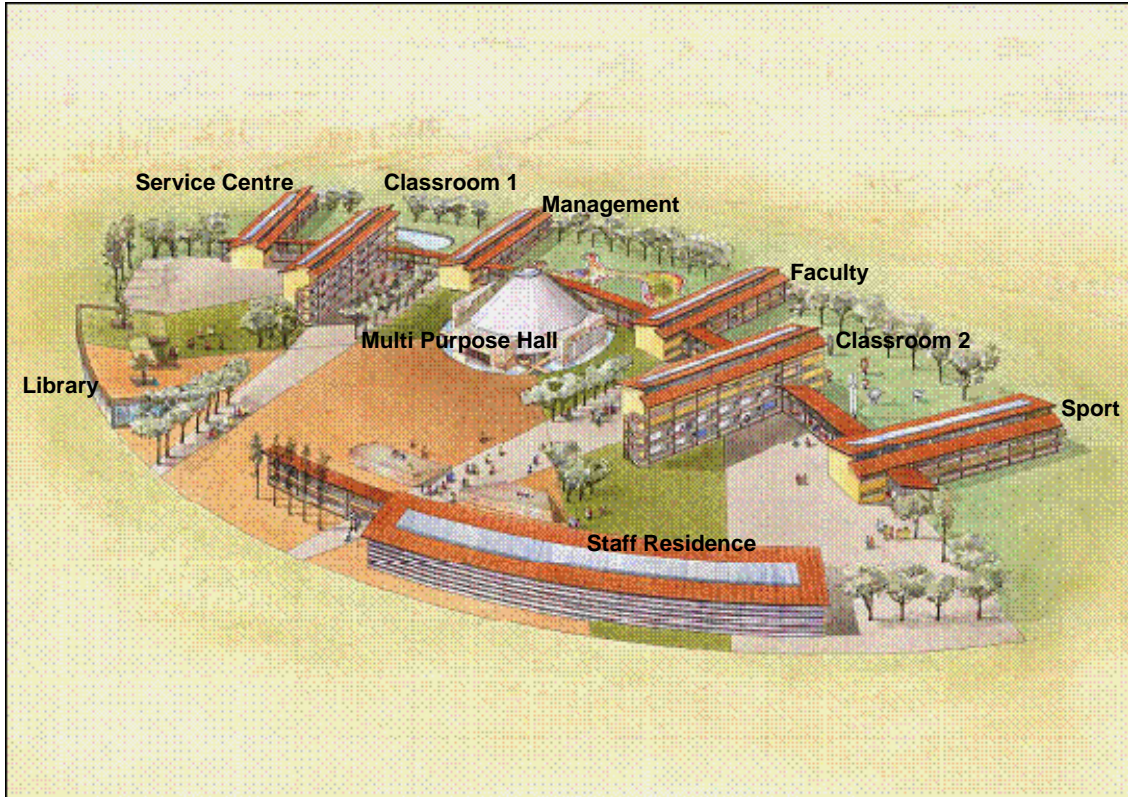

PROGRESS REPORT

Project : **Construction of Hope University College**
To : **Dr. Minas, Building Consortium (Holland), Ethiopiaid UK,
Menlo Park (USA), Ethiopiaid Ireland**
Date : **6 augustus 2008**
Prepared by : **Niek Hoffius**

The rainy season, which can last through mid September, has begun during the month of June. Almost no day passes without heavy rainfall, slowing down the production on site. Concrete work to the buildings of phase 1 (i.e. Service Centre, Classroom 1, Administration and Library) is, except the roof of the Library, the flat roof above the corridor and the beams supporting the metal roof of Classroom Building 2, almost finished.

Het regenseizoen, dat tot midden september kan duren, is in de maand juni begonnen. Er gaat bijna geen dag voorbij zonder hevige regenval, wat de productie op het werk vertraagt. Het betonwerk aan de gebouwen van fase 1 (dit zijn: Service Centre, Classroom 1, Administration en Library) is, met uitzondering van het dak van de Library, het platte dak boven de gang en de ondersteuningsbalken van het metalen dak van Classroom Building 2, bijna gereed.



Service Centre

Concrete work to the Service Centre is finished. Block (concrete) laying to the outside walls is in progress.

Het betonwerk van het Service Centre is gereed. Het metselen van de betonblokken voor de buitenmuren is aan de gang.



Classroom Building 1

Concrete work to the ground floor and the three storeys above is finished and the contractor has begun to erect the formwork to the (concrete) flat roof above the corridor of the third storey. At the right hand sight one of the sloped lecture halls on the second floor can be seen, the other lecture hall lies beneath ground level and is not visible on this picture.

Het betonwerk van de begane grondvloer en de drie verdiepingen daarboven is gereed en de aannemer is begonnen met het maken van de bekisting voor het platte dak boven de gang op de derde verdieping.

Rechts op de tweede verdieping is de hellende vloer van één van de collegezalen te zien, de andere collegezaal bevindt zich op de begane grond onder maaiveld en is daarom niet zichtbaar op deze foto.



Management Building

Concrete work to the Management Building is finished. Block (concrete) laying to the walls is in progress.

Het betonwerk van het Management Building is gereed. Het metselen van de betonblokken voor de wanden is aan de gang.



Faculty Office

The formwork with the reinforcement to the first floor is ready to receive concrete. After this floor is finished, the contractor will begin to cast the concrete columns which will support the roof. In the background the classroom building 1 can be seen.

De bekisting met het betonstaal van de eerste verdieping is gereed om beton te ontvangen. Nadat deze vloer gereed is, zal de aannemer beginnen om de betonnen kolommen te storten die het dak zullen ondersteunen. Op de achtergrond kan het classroom gebouw 1 worden gezien.



Classroom Building 2

The second floor (above the ground floor) of this building is almost ready.

De tweede verdieping is bijna gereed.



Knowledge Centre (Library)

The eucalypti's supports to the roof of the Knowledge Centre are being erected. After all the supports have been erected, the carpenters will cut them to the right length.

De eucalyptus ondersteuningen onder het dak van het Knowledge Centre worden overeind gezet. Nadat alle ondersteuningen overeind staan, zullen de timmerlieden beginnen met het afzagen op de juiste hoogte.



Staff Residence Building

The foundation is ready and the columns to the roof beam of the lower block are being erected. The Staff Residence Building consists of two blocks, one block with only a ground floor and 8 apartments and the second block consists of two floors with 16 apartments. The apartments are mainly meant for future staff personnel from abroad.

De fundatie is gereed en de kolommen onder de dakbalk worden gemaakt. Het Staff Residence Building bestaat uit twee blokken, één blok met slechts een begane grondvloer en 8 appartementen en het tweede blok bestaat uit twee vloeren met 16 appartementen. De appartementen zijn hoofdzakelijk bedoeld voor het toekomstige stafpersoneel uit het buitenland.
